Force Power Systems

116 Dickson Road
Houma, LA 70363
985-580-9978
info@forcepowersystems.com

Name	**NINE X POWER**	*Vehicle Serial No.*	**LLA01020**	*Work Order*	**4436677**
Engine Make	**CAT**	*Engine ID*		*Dyno Operator*	**CURTIS MOORE**
Engine Model	**3512**	*Engine Rating*	**1475HP@1200RPM**		

Operator Notes

BASE PRESSURE 1.2
LEFT BANK EXAUST TEMP 1108
RIGHT BANK EXAUST TEMP 1114
OIL TEMP 196

HRS 26366
FUEL BURN 491181

Other Comments

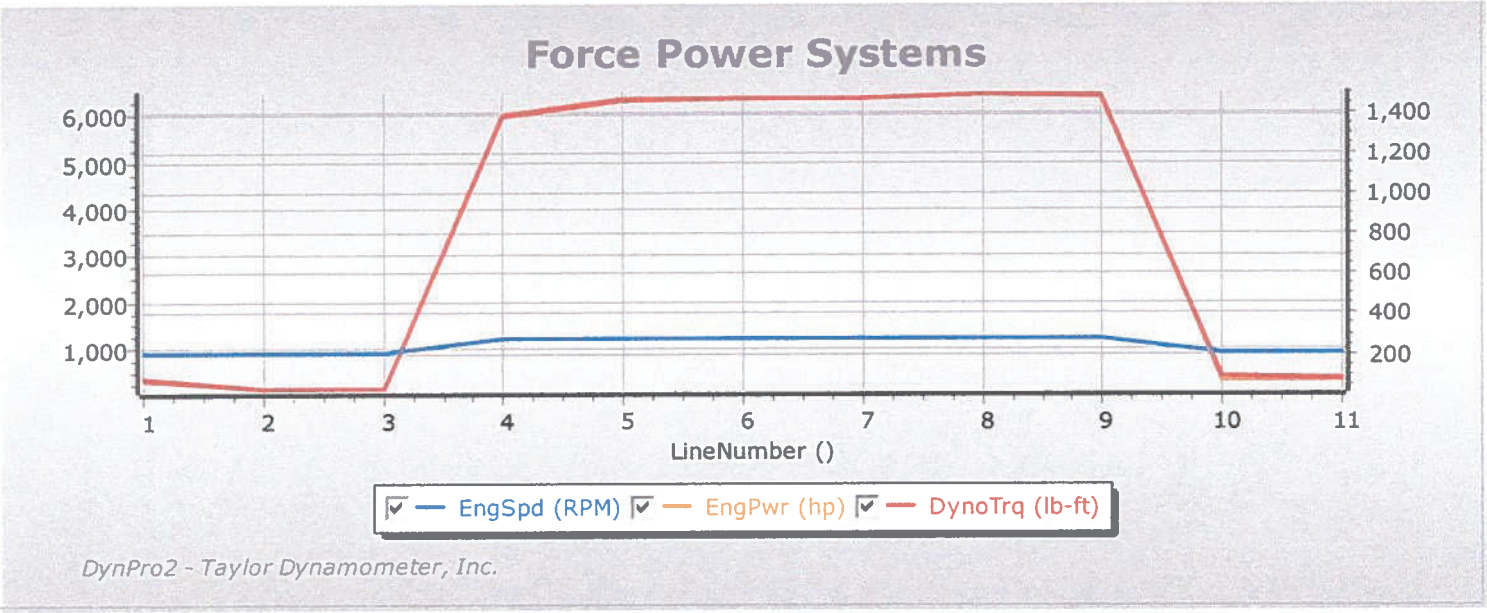

EngSpd (RPM)	EngPwr (hp)	DynoTrq (lb-ft)	OilP (psi)	CoolantT (° F)	FuelP (psi)	BoostP (psi)	ManualTestTime (min)
913	68.1	391.9	79.80	85	75.21	-0.73	0.2
913	27.3	157.3	71.08	143	75.24	-0.48	15.1
913	28.3	162.9	64.77	175	74.86	-0.31	30.1
1219	1388.3	5982.5	65.25	176	75.68	32.64	31.8

© Taylor Dynamometer, Inc. All Rights Reserved.
Test was performed on: 10/08/2026
File: 4436677 3512 NINEX POWER

Force Power Systems
116 Dickson Road
Houma, LA 70363
985-580-9978
info@forcepowersystems.com

EngSpd (RPM)	EngPwr (hp)	DynoTrq (lb-ft)	OilP (psi)	CoolantT (° F)	FuelP (psi)	BoostP (psi)	ManualTestTime (min)
1218	1464.8	6315.1	60.71	181	76.42	35.52	45.3
1216	1469.5	6346.9	59.92	182	76.26	35.18	60.6
1216	1471.0	6351.9	59.52	182	76.23	35.08	74.9
1214	1487.8	6437.4	59.14	182	75.71	35.21	90.2
1215	1483.9	6414.3	59.41	182	76.10	34.88	106.2
913	68.4	393.7	58.79	180	73.94	0.39	106.8
913	68.1	391.9	63.30	169	74.36	-0.27	121.1

© Taylor Dynamometer, Inc. All Rights Reserved.
Test was performed on: 10/08/2026
File: 4436677 3512 NINEX POWER
